


# Connect Hanover



## Hanover County Broadband Initiative August, 2022 Milestones

MILESTONE TIMELINE

GRANTEE Name: Hanover County  
 Contract Period: August 1, 2022 - August 1, 2024  
 Contract Number: VATISF#2022-021

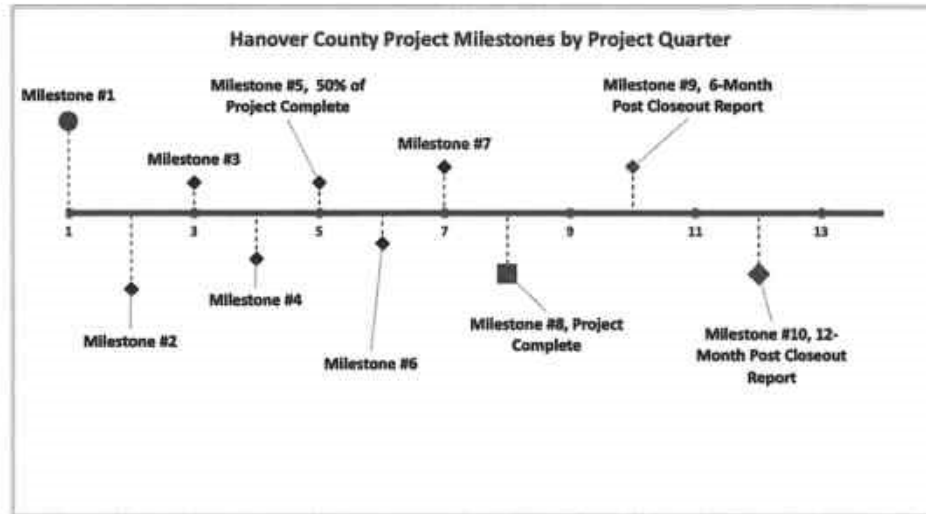

Milestone Number	End of Project Quarter	Miles Designed		Miles Constructed			Serviceable Units Passed		Project Complete to Date
		APB Miles Released to Date	% of Total	APB Constructed to Date	Utility Middle Mile Constructed to Date	% of Total	Passed to Date	% of Total	% Project Complete
1	1	50.0	11.3%	0.0	0.0	0.0%	0	0.0%	3.76%
2	2	110.0	24.8%	50.0	12.7	11.3%	702	11.3%	15.80%
3	3	170.0	38.3%	110.0	27.9	24.8%	1,545	24.9%	29.35%
4	4	230.1	51.9%	170.0	43.1	38.3%	2,388	38.5%	42.91%
5	5	310.1	69.9%	230.1	58.4	51.9%	3,231	52.1%	57.97%
6	6	390.1	87.9%	310.1	78.6	69.9%	4,355	70.3%	76.04%
7	7	443.6	100.0%	390.1	98.9	87.9%	5,339	86.1%	91.36%
8	8	443.6	100.0%	443.6	112.5	100.0%	6,198	100.0%	100.00%
Project Complete at Milestone 8									
9	10	6-Month Post Closeout Report							
10	12	12-Month Post Closeout Report							

Note: Approved method of "% Project Complete" may vary from Project Management Plan table.

**Construction Schedule - Milestone Progress to Date by Project Month**

End of Project Month	1	2	3	4	5	6	7	8	9	10	11	12	
APB Fiber Miles Designed	10.0	20.0	30.0	40.0	50.0	60.0	70.0	80.0	90.0	100.0	110.0	120.0	
APB Fiber Miles Constructed	0.0	0.0	0.0	10.0	20.0	30.0	40.0	50.0	60.0	70.0	80.0	90.0	
Utility Middle Miles Constructed	0.0	0.0	0.0	0.0	0.0	12.7	12.7	12.7	27.9	27.9	27.9	43.1	
Serviceable Units Passed	0	0	0	0	335	702	1050	1405	1545	1885	2110	2388	
End of Project Month	13	14	15	16	17	18	19	20	21	22	23	24	
APB Fiber Miles Designed	230.0	290.0	310.0	350.0	370.0	390.0	410.0	430.0	443.6	443.6	443.6	443.6	
APB Fiber Miles Constructed	190.0	210.0	230.0	250.0	260.0	270.0	280.0	290.0	300.0	310.0	320.0	330.0	
Utility Middle Miles Constructed	43.1	43.1	58.4	58.4	58.4	78.6	78.6	78.6	98.9	98.9	98.9	112.5	
Serviceable Units Passed	2705	3012	3234	3610	3982	4355	4710	5075	5339	5713	5923	6198	
